

From: Toliver, Aaron
Sent: Tuesday, November 20, 2012 1:34 PM
To: Leka, Kathy
Subject: FW: WAYNE COUNTY - NORFOLK CROSSING 724 725 D
Attachments: FINAL_PLANS_05124.pdf; 2012-11-16_Final Approach Estimate of Cost.pdf

Kathy, please file the attached e-mail status report and IDOT approved plans in T12-0062. Thanks.

From: David Connor [mailto:dconnor@connorengineers.com]
Sent: Monday, November 19, 2012 9:26 AM
To: Toliver, Aaron
Subject: RE: WAYNE COUNTY - NORFOLK CROSSING 724 725 D

Aaron,
Attached are the final approved plans.

From: Toliver, Aaron [mailto:atoliver@icc.illinois.gov]
Sent: Friday, November 16, 2012 1:20 PM
To: David Connor
Subject: RE: WAYNE COUNTY - NORFOLK CROSSING 724 725 D

David,

Please provide a PDF of the signed IDOT approved plans. Cover sheet and plan-profile/cross section pages are sufficient if scanning manually. Thanks very much.

Aaron Toliver

From: David Connor [mailto:dconnor@connorengineers.com]
Sent: Friday, November 16, 2012 1:14 PM
To: Toliver, Aaron
Subject: WAYNE COUNTY - NORFOLK CROSSING 724 725 D

Aaron,
The final plans have been approved by the Dept. of Transportation. Attached for your file is the final estimate of cost.
Please let me know if you need anything else.

STATE OF ILLINOIS
 DEPARTMENT OF TRANSPORTATION
 DIVISION OF HIGHWAYS
 PLANS FOR PROPOSED
 ROAD DISTRICT IMPROVEMENT
 GRADE CROSSING PROTECTION FUNDS
 WAYNE COUNTY
 SECTION 12-05124-00-AS
 BIG MOUND ROAD DISTRICT
 TR 394

INDEX OF SHEETS

- 1 COVER SHEET
- 2 PLAN & PROFILE
- 3 CROSS SECTIONS


STANDARDS:
 (SEE PROPOSAL) 701901-02 - TRAFFIC
 BLR 21-9 - TRAFFIC

SCALES

- PLAN 1 INCH = 50 FEET
- PROFILE HORZ. 1 INCH = 50 FEET
- PROFILE VERT. 1 INCH = 10 FEET
- CROSS SECTIONS 1 INCH = 5 FEET

SUMMARY OF QUANTITIES

QUANTITY	UNIT	ITEM
100	CU YD	EARTH EXCAVATION
132	CU YD	FURNISHED EXCAVATION
453	TON	AGGREGATE BASE COURSE, TYPE B
54	FOOT	PIPE CULVERTS, CLASS D, TYPE 1, 24"
54	FOOT	PIPE CULVERTS, CLASS D, TYPE 1, 30"
22	CU YD	CONTROLLED LOW STRENGTH MATERIAL
1	L SUM	TRAFFIC CONTROL AND PROTECTION
1	L SUM	RAILROAD PROTECTIVE LIABILITY INSURANCE
48	FOOT	PIPE CULVERT REMOVAL
72	SQ YD	PAVEMENT REMOVAL

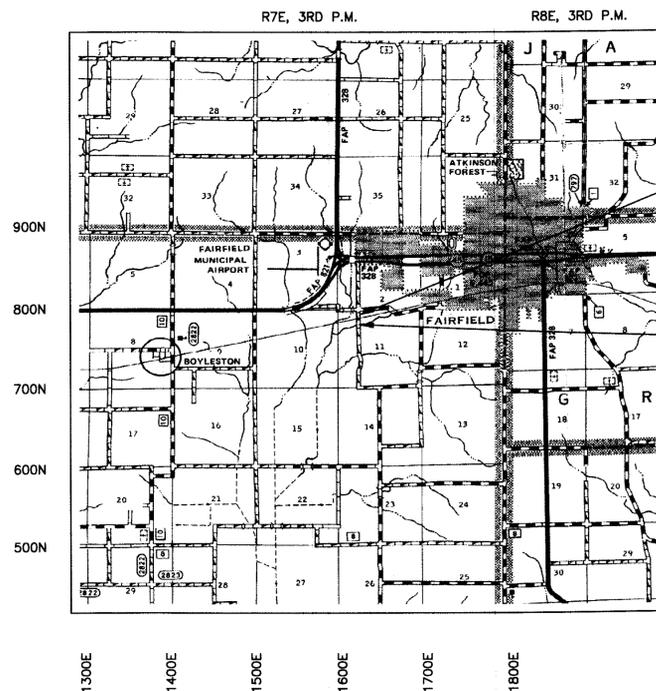

SECTION 12-05124-00-AS
 ENDS STA. 5+49

OMISSION FOR RAILROAD
 STA. 3+11 TO STA. 3+19

SECTION 12-05124-00-AS
 BEGINS STA. 0+65

FUNCTIONAL CLASS: RURAL LOCAL ROAD
 ADT = 50
 DESIGN SPEED = 30 MPH

LOCATION MAP

APPROXIMATE SCALE: 1 INCH = 1 MILE
 TOTAL LENGTH = 484 FT. = 0.092 MILES
 OMISSION FOR RAILROAD = 8 FT. = 0.002 MILES
 NET LENGTH = 476 FT. = 0.090 MILES



John A. Storie 10/30/2012
 ILLINOIS REGISTERED PROFESSIONAL ENGINEER # 55012
 LICENSE EXPIRES NOVEMBER 30, 2013

PROFESSIONAL DESIGN FIRM #184-000832







TOLL FREE JOINT UTILITY LOCATING
 INFORMATION FOR EXCAVATORS (J.U.L.I.E.)
 TELEPHONE NO. 1-800-892-0123



WAYNE COUNTY HIGHWAY DEPARTMENT	
APPROVED:	<i>Greg Hirsch</i> 10/30 . 2012 WAYNE COUNTY ENGINEER
PASSED:	<i>Mamen E. Kault</i> 11-7 . 2012 DISTRICT SEVEN ENGINEER OF LOCAL ROADS & STREETS
RELEASING FOR BID BASED ON LIMITED REVIEW	<i>Rozar Z. Anshel</i> 11-7 . 2012 DEPUTY DIRECTOR OF HIGHWAYS, REGION FOUR ENGINEER

HERSCHEL L. HIDGON
TRUSTEE OF HERSCHEL L. HIDGON REMOVABLE TRUST

SECTION	12-05124-00-AS	TOTAL SHEETS	3	SHEET NO.	2
COUNTY	WAYNE	ROAD DIST.	BIG MOUND	STA. 0+00	TO STA. 6+49.50

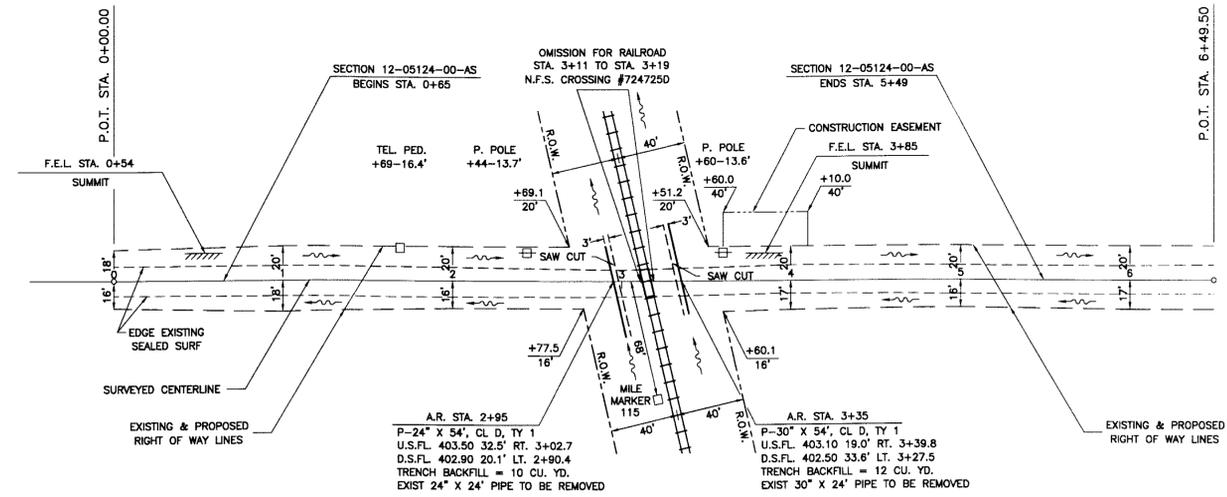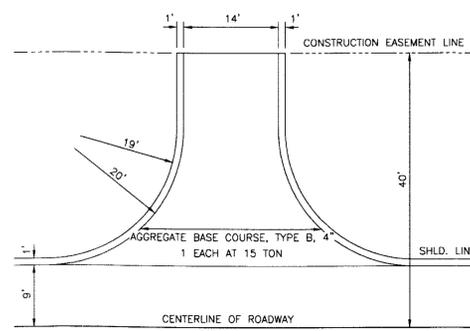

VERNON & MARY LOU GWALTNEY

EARTHWORK SCHEDULE

EARTH EXCAVATION	=	100 CU. YD.
EARTH EXCAVATION ADJUSTED 25%	=	75 CU. YD.
EMBANKMENT	=	207 CU. YD.
FURNISHED EXCAVATION	=	132 CU. YD.

B.M. #1 ELEVATION 404.36
P.K. IN POWER POLE
LT. STA. 0-20

SEEDING TO BE DONE BY OTHERS

PIPE CULVERT REMOVAL

A.R. STA. 2+95	=	24 FOOT
A.R. STA. 3+35	=	24 FOOT
TOTAL	=	48 FOOT

AGGREGATE BASE COURSE, TYPE B

STA. 0+65 TO STA. 3+11	=	226 TON
STA. 3+19 TO STA. 5+49	=	212 TON
F.E.L. STA. 3+85	=	15 TON
TOTAL	=	453 TON

PAVEMENT REMOVAL

STA. 2+78 TO STA. 2+98	=	36 SQ YD
STA. 3+32 TO STA. 3+52	=	36 SQ YD
TOTAL	=	72 SQ YD

UTILITIES

TELEPHONE: FRONTIER	ELECTRIC: WAYNE-WHITE ELECTRIC
225 E. CHESTNUT ST.	RT. 45 WEST
OLNEY, IL 62450	FAIRFIELD, IL 62837
618-395-6189	618-842-2198

CONNOR & CONNOR, Inc.
CONSULTING ENGINEERS
210 East Locust Street
ROBINSON, ILLINOIS 62454
Phone: 618-544-8673 Fax: 618-544-3012
Licensed Surveyors

DATE: 5/10/2012
SCALE: 1" = 50'
DRAWN BY: J.C.
PROJECT: P-1626
SHEET: OF

